

New Product Management (NPM) Module

Guideline

Objective: To ensure on-time product launching by identifying and resolving loophole

Stepwise Journey Guideline:


Dashboard: Under development stage with Test & Trial by end users.

Proposal: Under development stage with Test & Trial by end users.

Format: Under development stage with Test & Trial by end users.

Gantt chart: It will generate automatically by calculating SOP timeline for product launching process under 8 main activities. And the counting will start from the approval date of COO Sir. These 8 main activities will run upon different sub-activities of the **Process Report** section. There will display option for two separate timeline-

- Standard Timeline: It will generate automatically upon SOP timeline.
- Deviated Timeline: It will generate based on deviation of SOP timeline.

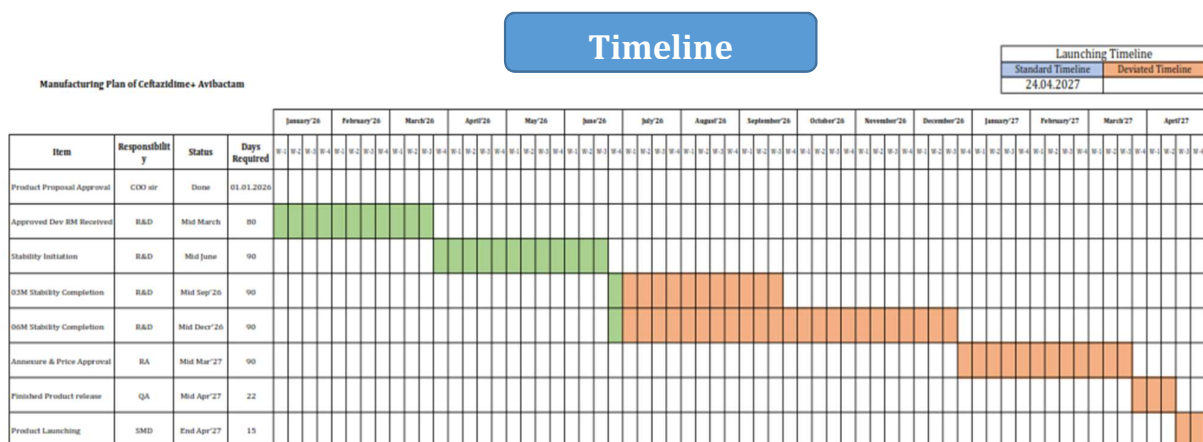

Process Report: This section is the showcase of all activities in a single table, required for the completion of total launching process. Here, the activities will run one after another. After COO Sir's approval notification will go to concerned persons of SMD, R&D, SCM & RA departments. While one activity will complete notification will go to concerned person of next activity and activity color will remain red unless it is done. When it is done, then activity will be colorless and next pending activity will be red colored.

In **Process Report** table green colored activity related documents must be uploaded and will be compiled to respective folder in **New Product Document**. Rest documents are not required to upload, if uploaded it will go to folder named *Miscellaneous* in **New Product Document**.

[illegible]

Notification will display in **Dashboard** section of concerned person. Like-

Metric	Value
Internal Product Brief	4
6M Forecast	4
Internal Brand Name	3
Packaging Concurrence	3
Internal Price	4
AFPC Doc	0
Launching Circular	0

When one person click on **Dashboard** bar of specific pending activity, then a table on respective activity will be visible for uploading required documents (if available).

Internal Product Brief								
Sl. No.	Generic Code	Product Code	Generic Name	Strength	Dosage Form	Launching	Action	Comment
1	NP06260018	NP06260018 (a)	Sitagliflozin	150mg	Tab	01.04.2027	☐ Yes ☐ Pending Upload	
2	NP06260015	NP06260015 (a)	Aceclofenac	200mg	Tab	01.12.2026	☐ Yes ☐ Pending Upload	
3	NP06260014	NP06260014 (a)	Ceftazidime+ Avibactam	1.25g	Inj	01.04.2027	☐ Yes ☐ Pending Upload	
4	NP06260014	NP06260014 (b)	Ceftazidime+ Avibactam	2.5g	Inj	01.02.2027	☐ Yes ☐ Pending Upload	

When concerned person will click on **Yes** button and upload required documents, then the input date will be showcased at respective activity box in **Process Report** section and red color will shift to next activity box as the reflection of pending activity.

If the person click on **Pending** button, he/she has to give comment with reason behind pending. This comment will display as notification icon at respective activity box in **Process Report** section. And these icons will remain visible.

SBU	Generic	Therapeutic Class	Strength	Dosage Form	Product Category	Unit Forecast (Y-1)	Value Forecast (Y-1)	Launching Date	PP Code	PP Date	Plant	PP Approved On	Duration (PP to PP Approval)	Product Brief (PB) Sharing On	Product Forecast (PF) Sharing On	Dev RM specification to SCM by R&D Date	Dev RM Received
Pharma Common	Lacosamide	Antiepileptic	50mg	Tablet	New Molecule			01.04.27	NP-0125-0001	07.01.2025	NG	01.01.26	34	12.03.2025	14.03.2025	Date	09.03.2025

Method Dev. & Stability Initiation	3M Stability Completion	Recipe Submission to RA Date	Duration (PP Approval to Recipe Submission)	Recipe Approved On	DTL shared to RA by R&D on	PM Spec Shared to SMD by R&D	Tooling/Machine/Change parts PR to SCM by R&D/Eng Date	RM/PM requisition to SCM by R&D	DTL Approval Date	Brand Name & PM Design to RA Date	Duration (PM Spec Sharing to PM Design to RA)	Price Submission to RA Date	6M Stability Completion	Annexure Documents to RA by R&D Date	Tooling/Machine/Change parts Availability at Plant	Brand Name & PM Design Approval by DA	Annexure Approval by DA Date
25.04.2025		07.08.2025	175	25.09.2025	Date/NA	01.10.2025	Date/NA	Date	Date/NA	20.09.2025	05.10.2025	10.10.2025		Date	Date/NA	15.10.2025	10.11.2025

Inclusion Approval by DA Date	PM Design Delivery to Vendor by SCM Date	PM Machine Proof Approval From QC Date	Commercial RM Received On	Commercial PM Received On	Technology Transfer	Duration (Annexure Approval to Commercial PM Received)	Price Approval by DA Date	MA Sample to RA by R&D	Finished Product Released	MA Certificate Received On	Product Launching Date	Duration (Price Approval to Product Launching)	PP Creator	Remarks
	30.11.2025	30.11.2025	20.12.2025	15.12.2025		34	25.11.2025	10.01.2026		10.01.2026	01.02.2026	68	Saif Ahmed	

When a person click on notification icon, all previous comments will be visible with current one so that one can see all reasons behind delay of launching process in single click.

Departments	Items	Upload	Date	Remarks
PP creator	Product Brief (PB) Sharing to R&D On	Internal Product Brief	12.02.26	Waiting for originator product
	Product Forecast (PF) Sharing On	Product Forecast	15.02.26	Waiting for COO Sir's approval
	Brand Name & PM Design to RA	Internal Brand Name Packaging Concurrence		
	Price Submission to RA	Internal Price		
	Product Launching	Launching Circular		
R&D	Dev RM specification to SCM by R&D	Dev. RM Spec. Sharing		
	Dev RM Received	Dev RM Receive	10.05.26	SCM Couldn't manage DEV RM yet
			26.05.26	Due to high cost SCM couldn't manage Dev RM yet
	Method Dev. & Stability Initiation	Formulation Concurrence		
	3M Stability Completion	3M Stability Completion		
	Recipe Submission to RA	Recipe Doc. Sharing		
	DTL shared to RA by R&D on	DTL Doc. Sharing		
	Approved Product Brief (PB) Sharing On	Approved Product Brief	10.07.26	Need spec. correction
	PM Spec Shared to SMD by R&D	PM Spec. Sharing		

New Product Calendar: This section will showcase month wise yearly new product launching plan. This month wise yearly plan will generate automatically by counting “*Launching Month*” from tentative forecast table in “**Product Proposal Form**”.

This calendar will display yearly launching plan under four categories-

- NG (New Molecule);
- NG (Line Extension);
- AHL (New Molecule) and
- AHL (Line Extension)

For those products crossing SOP timeline will be highlighted with red color.

New Product (New Molecule+Line Extension) Calendar

NI	2	6	8	2	3	3	3	3	4	5	4
AHL	1	5	3	0	6	1	0	3	5	5	1
Total	3	11	11	2	9	4	3	6	9	10	5
Plant	Nov-25	Dec-25	Jan-26	Feb-26	Mar-26	Apr-26	May-26	Jun-26	Jul-26	Aug-26	Sep-26
N.G. (New)	Rivarogine 1.5mg, 3mg & 4.5mg Cap (Priority: A) Shelfed from Apr-25	Sitagliptin 200mg tab (Shelfed from May-25)	Vortioxetine 5mg & 10mg Tab (Shelfed from May-25)	Tubogrip 15mg Tab (Shelfed from Aug-25)	Cibataad Propionate-Salicylic Acid 0.05% - 3% Oint.	Lorazepam 4mg & 8mg Tab	Lidocaine 1% Cream	Acetaminide 100mg Tab TSC 255 rejected	Sucralgine 50mg Tab Depends on DCC (Recipe TBS)	Endoloxine 300mg Cap & 175mg/ml Sus (Shelfed from Jun-25)	Acetaminide 350mg Tab Depends on DCC (Recipe TBS)
		Bilastine 20mg Tab 12.5mg/ml O/S (Priority: A-) Shelfed from May-25	Docagliflozin 20mg Tab (DCC 254) (Shelfed from Jul-25)		Stafloxacin 50mg & 100mg Tab (100mg DCC dependent)	Ectocaine 2% Shampoo	Ciprofloxacin 100mg Tab	Braconazole 65mg & 100mg Cap.	Acetaminide + Paracetamol 154+27.5mg/Spray N.Spray Depends on DCC (TSC 2, No comment)	Sarglaxar Magnesium 2mg Tab (Shelfed from Jun-25)	Endoloxine 300mg 2.5ml tab Sus Depends on DCC-TSC 2 (Recipe TBS)
		Osetipitant 45mg Tab	Lacosamide 50mg & 100mg Tab (Shelfed from Dec-25)			Vibegron 50mg Tab (Shelfed from Nov-25) Add Acetaminide (0.05% DCC 254)		Braconazole + Tubogrip 200mg/250mg Tab.		Braconazole 100mg D.F. Inj Depends on DCC (TSC 2)	
			Ranolazine 500mg & 750mg TR Tab (Priority: B) Shelfed from Mar-25								
			Cefazolin + Avibactam 2g+0.5g D.F. Inj (Shelfed from Dec-25)								


New Product Documents: This section will showcase all documents uploaded by concerned persons during different activity run. Molecule wise product list will be displayed in a table.

Sl. No.	Molecule Code	Product Code	Molecule	Therapeutic Class	Strength	Dosage Form	Annexure Issue Date	Annexure Expiry Date	Document
1	NP06260001	NP06260001 (a)	Ceftazidime + Avibactam	Antibiotic	2.5g	Injection	10.06.2026	10.06.2029	Unlock

“Annexure Issue Date” & “Annexure Expiry Date” will be tracked from the table filled during Annexure upload by concerned Regulatory person.

Annexure Approval										
Sl. No.	Generic Code	Product Code	Generic Name	Strength	Dosage Form	Launching	Annexure Issue Date	Annexure Expiry Date	Action	Comment
1	NP06260018	NP06260018 (a)	Sitagliptin	150mg	Tab	01.04.2027			☐ Yes ☐ Pending Upload	
2	NP06260015	NP06260015 (a)	Aceclofenac	200mg	Tab	01.12.2026			☐ Yes ☐ Pending Upload	
3	NP06260014	NP06260014 (a)	Ceftazidime+ Avibactam	1.25g	Inj	01.04.2027			☐ Yes ☐ Pending Upload	
4	NP06260014	NP06260014 (b)	Ceftazidime+ Avibactam	2.5g	Inj	01.02.2027			☐ Yes ☐ Pending Upload	

When PP creator press the **Unlock** button a different screen will open with Generic name.

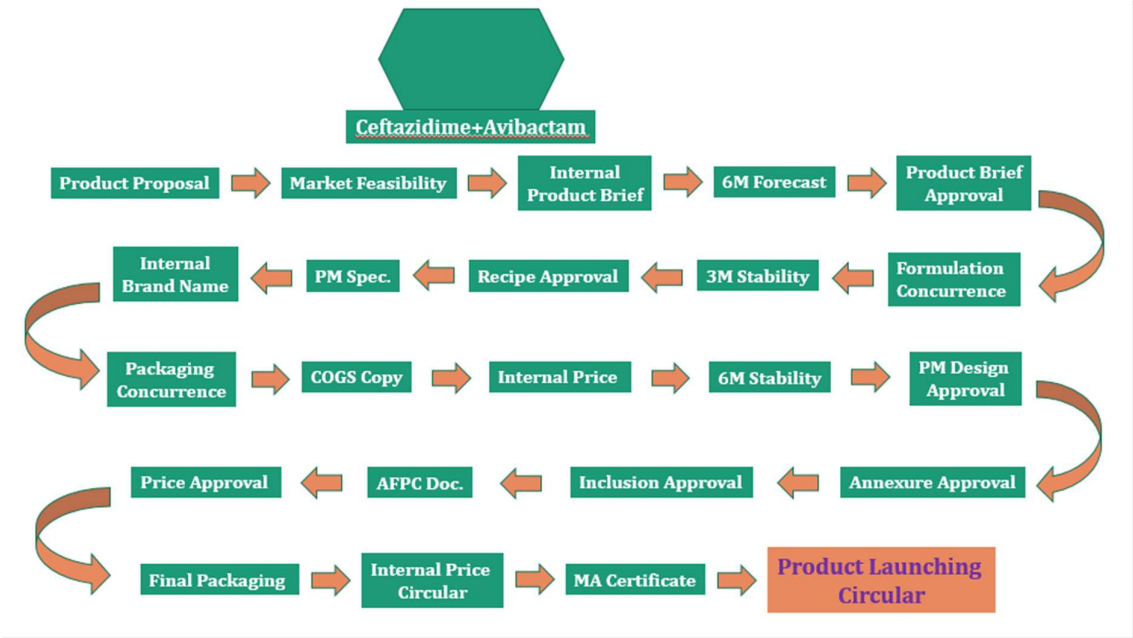

In this section, all uploaded documents will be compiled in different folders by their name. Once a document is uploaded respective folder color will be turned to green. End users have a 30-minute window to delete it themselves. After that, deletion requires approval from MIS.
